Appendix 2.1 Tentative Construction Programme

Activity ID	Description	Start Date	End Date
1	**Revised Trunk Road T4 in Sha Tin**		
2	**(A) Work Zone at Northern Side of Shing Mun River**		
3	**(A1) Work Zone A1**		
4	(A1.1) Site Clearance / Set-up / Plant Mobilization / Tree Felling and Transplanting Works	02-2024	02-2024
5	(A1.2) Utilities Protection and Diversion Works	03-2024	03-2024
6	(A1.3) Slopework	04-2024	05-2024
7	**(A1.4) Construction of Bridge Structure for Slip Road SR1-1 connecting SMTR(EB)**		
8	(A1.4.1) Piling Works	06-2024	09-2024
9	(A1.4.2) Pile Caps and Piers	10-2024	02-2025
10	(A1.4.3) Bridge Deck	03-2025	07-2025
11	(A1.4.4) Roadworks, Drainage & Utilities	08-2025	09-2025
12	(A1.4.5) Pavement	10-2025	10-2025
13	**(A1.5) Construction of Bridge Structure for T4(EB) Slip Road SR2-1**		
14	(A1.5.1) Piling Works	11-2024	03-2025
15	(A1.5.2) Pile Caps and Piers	04-2025	09-2025
16	(A1.5.3) Bridge Deck	02-2027	04-2027
17	(A1.5.4) Roadworks, Drainage & Utilities	05-2027	06-2027
18	(A1.5.5) Pavement	04-2028	04-2028
19	**(A1a) Work Zone A1a**		
20	(A1a.1) Slopework	06-2024	07-2024
21	(A1a.2) Roadworks & Pavement	10-2025	10-2025
22	**(A2) Work Zone A2**		
23	(A2.1) Site Clearance / Set-up / Plant Mobilization / Tree Felling and Transplanting Works	09-2024	09-2024
24	(A2.2) Utilities Protection and Diversion Works	10-2024	10-2024
25	**(A2.3) Construction of Bridge Structure for T4(EB) Slip Road SR2-1**		
26	(A2.3.1) Piling Works	10-2025	02-2026
27	(A2.3.2) Pile Caps and Piers	03-2026	08-2026
28	(A2.3.3) Bridge Deck	10-2026	01-2027
29	(A2.3.4) Temporary Removal of Existing Noise Barrier	10-2026	10-2026
30	(A2.3.5) Reprovision of Noise Barrier	02-2027	03-2027
31	(A2.3.6) Roadworks, Drainage & Utilities	07-2027	08-2027
32	(A2.3.7) Pavement	04-2028	04-2028
33	**(A2.4) Construction of Bridge Structure for T4(EB) Slip Road SR3-1**		
34	(A2.4.1) Piling Works	05-2025	09-2025
35	(A2.4.2) Pile Caps and Piers	10-2025	03-2026
36	(A2.4.3) Bridge Deck	07-2026	09-2026
37	(A2.4.4) Modification of Existing Bridge Structure of Tsing Sha Highway for Connection	10-2026	12-2026
38	(A2.4.5) Temporary Removal of Existing Noise Barrier / Enclosure	09-2026	09-2026
39	(A2.4.6) Reprovision of Noise Barrier / Enclosure	01-2027	02-2027
40	(A2.4.7) Roadworks, Drainage & Utilities	03-2027	04-2027
41	(A2.4.8) Pavement	04-2028	04-2028
42	**(A2.5) Modification of At-grade Roads**		
43	(A2.5.1) Roadworks, Drainage & Utilities	11-2024	03-2025
44	(A2.5.2) Pavement	04-2025	04-2025
45	**(A2a) Work Zone A2a**		
46	(A2a.1) Roadworks & Pavement	05-2027	05-2027
47	**(A3) Work Zone A3**		
48	(A3.1) Site Clearance / Set-up / Plant Mobilization / Tree Felling and Transplanting Works	10-2024	10-2024
49	(A3.2) Utilities Protection and Diversion Works	11-2024	11-2024
50	**(A3.3) Construction of Bridge Structure for T4(EB)**		
51	(A3.3.1) Piling Works	05-2025	09-2025
52	(A3.3.2) Pile Caps and Piers	10-2025	03-2026
53	(A3.3.3) Bridge Deck	04-2026	06-2026
54	(A3.3.5) Noise Barriers	07-2027	09-2027
55	(A3.3.6) Roadworks, Drainage & Utilities	09-2027	10-2027
56	(A3.3.7) Pavement	04-2028	04-2028
57	**(A3.4) Modification of SMTR(EB) (Bridge Structure)**		
58	(A3.4.1) Piling Works	04-2026	08-2026
59	(A3.4.2) Pile Caps and Piers	09-2026	02-2027
60	(A3.4.3) Bridge Deck	03-2027	08-2027
61	(A3.4.4) Modification of Existing Reserved T4 Connection Point A (CP-A)	06-2027	07-2027
62	(A3.4.5) Temporary Removal of Existing Noise Barrier	06-2027	06-2027
63	(A3.4.6) Noise Barriers	09-2027	11-2027
64	(A3.4.7) Roadworks, Drainage & Utilities	11-2027	12-2027
65	(A3.4.8) Pavement	01-2028	01-2028
66	**(A3.5) Modification of At-grade Roads**		
67	(A3.5.1) Roadworks, Drainage & Utilities	12-2024	04-2025
68	(A3.5.2) Pavement	05-2025	05-2025
69	**(A3a) Work Zone A3a**		
70	(A3a.1) Roadworks & Pavement	08-2027	08-2027

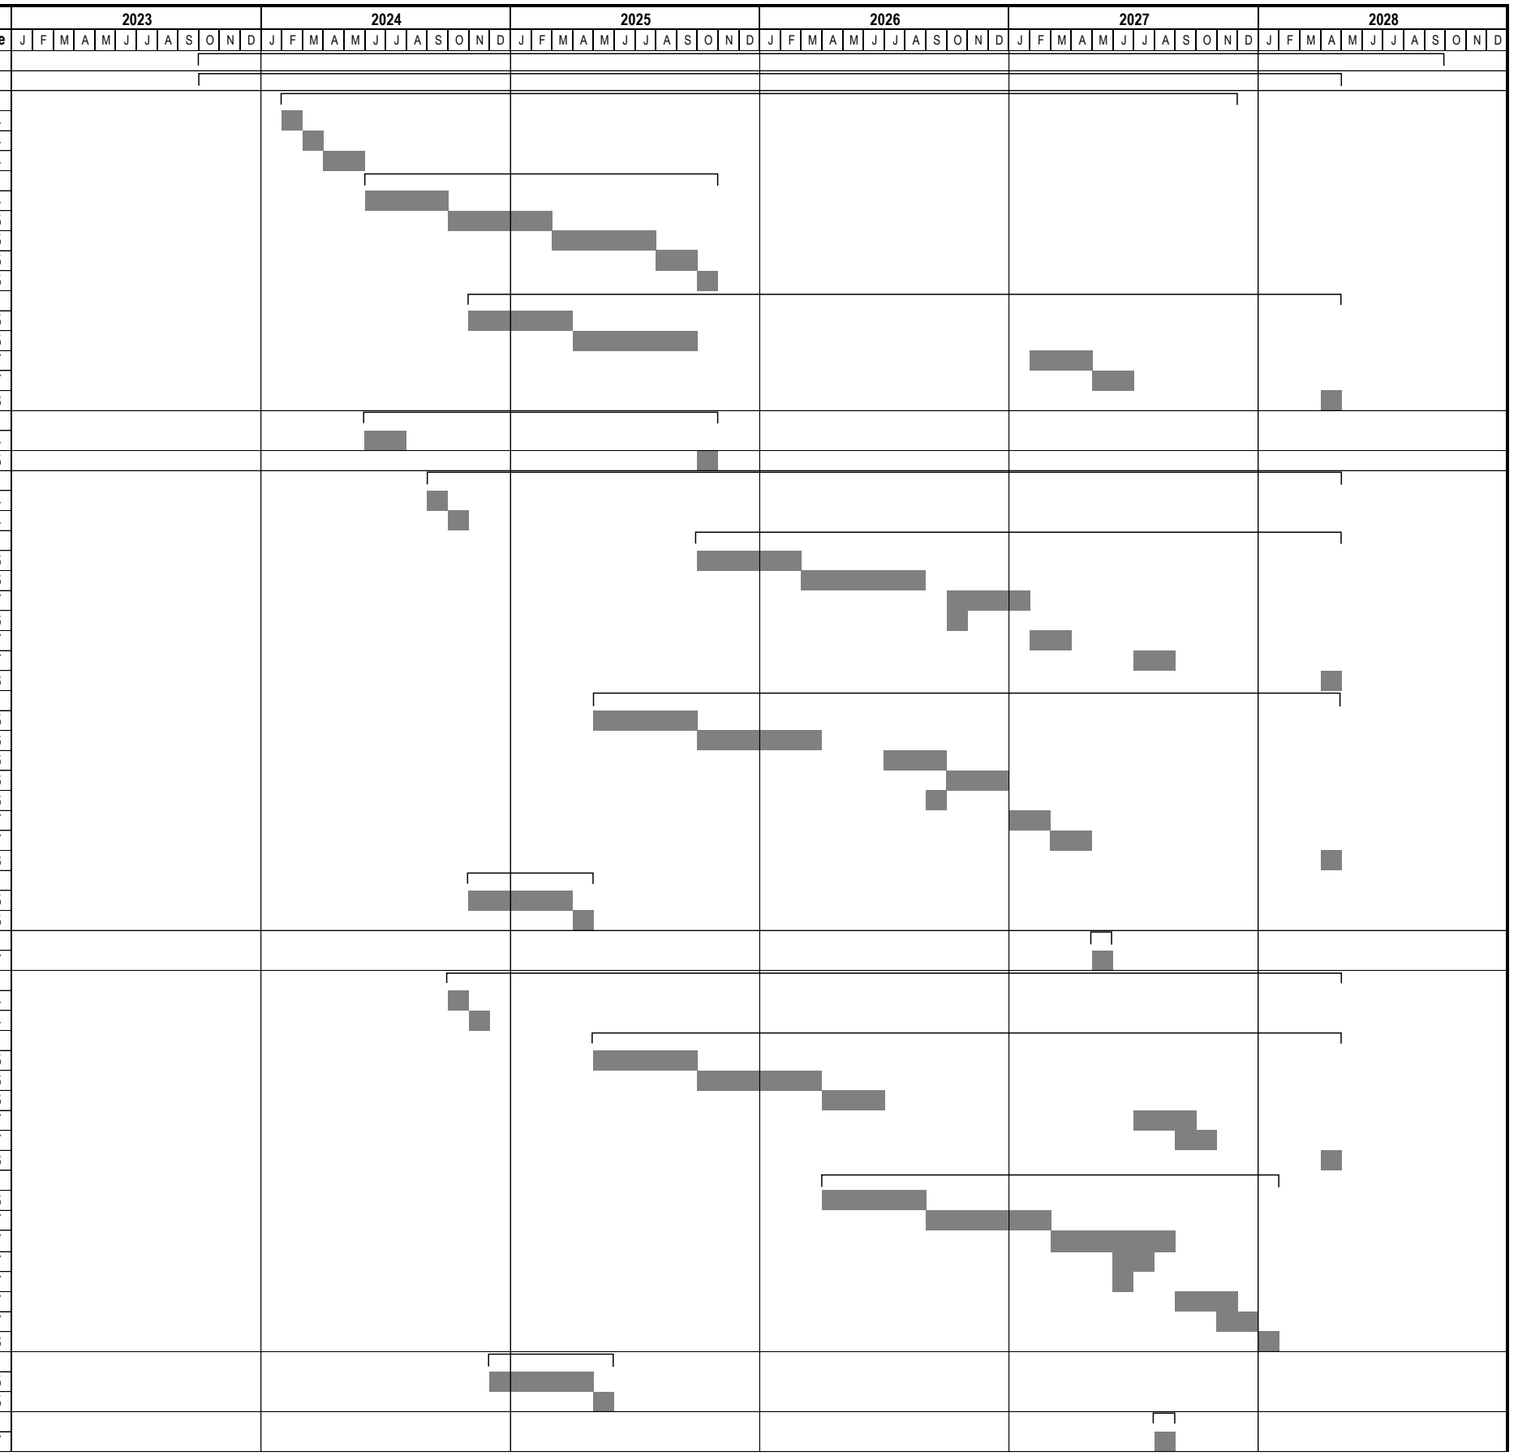

Appendix 2.1 Tentative Construction Programme

Activity ID	Description	Start Date	End Date
71	**(A4) Work Zone A4**		
72	(A4.1) Site Clearance / Set-up / Plant Mobilization / Tree Felling and Transplanting Works	03-2024	03-2024
73	(A4.2) Utilities Protection and Diversion Works	04-2024	05-2024
74	**(A4.3) Construction of Bridge Structure for T4(EB)**		
75	(A4.3.1) Piling Works	06-2024	10-2024
76	(A4.3.2) Pile Caps and Piers	11-2024	04-2025
77	(A4.3.3) Bridge Deck	01-2026	03-2026
78	(A4.3.4) Noise Barriers / Enclosures	09-2027	11-2027
79	(A4.3.5) Roadworks, Drainage & Utilities	11-2027	12-2027
80	(A4.3.6) Pavement	04-2028	04-2028
81	**(A4.4) Construction of Bridge Structure for T4(WB) Slip Road SR4-1**		
82	(A4.4.1) Piling Works	12-2024	04-2025
83	(A4.4.2) Pile Caps and Piers	05-2025	10-2025
84	(A4.4.3) Bridge Deck	08-2026	10-2026
85	(A4.4.4) Modification of Existing Reserved T4 Connection Point B (CP-B)	11-2026	12-2026
86	(A4.4.5) Temporary Removal of Existing Noise Barrier	11-2026	11-2026
87	(A4.4.6) Reprovision of Noise Barrier	01-2027	02-2027
88	(A4.4.7) Noise Barriers / Enclosures	09-2027	11-2027
89	(A4.4.8) Roadworks, Drainage & Utilities	11-2027	12-2027
90	(A4.4.9) Pavement	04-2028	04-2028
91	**(A4.5) Construction of Bridge Structure for T4(WB) Slip Road SR5-1**		
92	(A4.5.1) Piling Works	06-2025	10-2025
93	(A4.5.2) Pile Caps and Piers	11-2025	04-2026
94	(A4.5.3) Bridge Deck	05-2026	07-2026
95	(A4.5.4) Modification of Existing Reserved T4 Connection Point C (CP-C)	08-2026	09-2026
96	(A4.5.5) Noise Barriers / Enclosures	09-2027	11-2027
97	(A4.5.6) Roadworks, Drainage & Utilities	11-2027	12-2027
98	(A4.5.7) Pavement	04-2028	04-2028
99	**(A5) Work Zone A5**		
100	(A5.1) Site Clearance / Set-up / Plant Mobilization	10-2023	10-2023
101	**(A5.2) Construction of Bridge Structure for T4(EB) and T4(WB) and Sip Road to LRTR across SMRC**		
102	(A5.2.1) Construction of Temporary Working Platform (South Portion)	11-2023	02-2024
103	(A5.2.2) Piling Works at SMRC (South Portion)	03-2024	04-2024
104	(A5.2.3) Pile Caps and Piers at SMRC (South Portion)	06-2024	09-2024
105	(A5.2.4) Construction of Temporary Working Platform (North Portion)	11-2024	02-2025
106	(A5.2.5) Piling Works at SMRC (North Portion)	03-2025	04-2025
107	(A5.2.6) Pile Caps and Piers at SMRC (North Portion)	06-2025	09-2025
108	(A5.2.7) Bridge Deck at SMRC	10-2025	12-2025
109	(A5.2.8) Modification of Existing Lion Bridge Structures for Slip Road Connection	11-2025	01-2026
110	(A5.2.9) Noise Barriers / Enclosures	12-2027	02-2028
111	(A5.2.10) Roadworks, Drainage & Utilities	02-2028	03-2028
112	(A5.2.11) Pavement	04-2028	04-2028
113	**(A5.3) Construction of Cycle Track cum Footbridge across SMRC**		
114	(A5.3.1) Construction of Temporary Working Platform (South Portion)	11-2023	02-2024
115	(A5.3.2) Piling Works at SMRC (South Portion)	05-2024	05-2024
116	(A5.3.3) Pile Caps and Piers at SMRC (South Portion)	10-2024	11-2024
117	(A5.3.4) Construction of Temporary Working Platform (North Portion)	11-2024	02-2025
118	(A5.3.5) Piling Works at SMRC (North Portion)	05-2025	05-2025
119	(A5.3.6) Pile Caps and Piers at SMRC (North Portion)	02-2026	03-2026
120	(A5.3.7) Bridge Deck at SMRC	04-2026	06-2026
121	**(B) Work Zone at Southern Side of Shing Mun River**		
122	**(B1) Work Zone B1**		
123	(B1.1) Site Clearance / Set-up / Plant Mobilization / Tree Felling and Transplanting Works	04-2025	05-2025
124	(B1.2) Utilities Protection and Diversion Works	06-2025	08-2025
125	**(B1.3) Construction of Depressed Roads for T4(EB) and T4(WB) and Slip Road to LRTR**		
126	(B1.3.1) Temporary Works for ELS	05-2027	09-2027
127	(B1.3.2) Excavation	10-2027	11-2027
128	(B1.3.3) Structures for Depressed Roads	12-2027	05-2028
129	(B1.3.4) Noise Barriers / Enclosures	06-2028	07-2028
130	(B1.3.5) Roadworks, Drainage, E&M Works	07-2028	08-2028
131	(B1.3.6) Pavement	09-2028	09-2028
132	**(B1.4) Construction of Cycle Track cum Footbridge**		
133	(B1.4.1) Piling Works	10-2027	11-2027
134	(B1.4.2) Pile Caps ad Piers	12-2027	02-2028
135	(B1.4.3) Bridge Deck	03-2028	05-2028
136	(B1.4.4) Cycle Track, Footpath and Landscape Works	06-2028	07-2028
137	**(B1a) Work Zone B1a**		
138	(B1a.1) Site Clearance / Set-up / Plant Mobilization / Tree Felling and Transplanting Works	11-2026	12-2026
139	(B1a.2) Utilities Protection and Diversion Works	01-2027	03-2027
140	**(B1a.3) Construction of Cycle Track cum Footbridge**		
141	(B1a.3.1) Piling Works	04-2027	05-2027
142	(B1a.3.2) Pile Caps ad Piers	06-2027	07-2027
143	(B1a.3.3) Bridge Deck	08-2027	09-2027
144	(B1a.3.4) Associated Structures (Ramp, Stairs & Lifts)	10-2027	01-2028
145	(B1a.3.5) Associated Structures for Cycle Track and Footpath	02-2028	06-2028
146	(B1a.3.6) Cycle Track, Footpath and Landscape Works	07-2028	08-2028

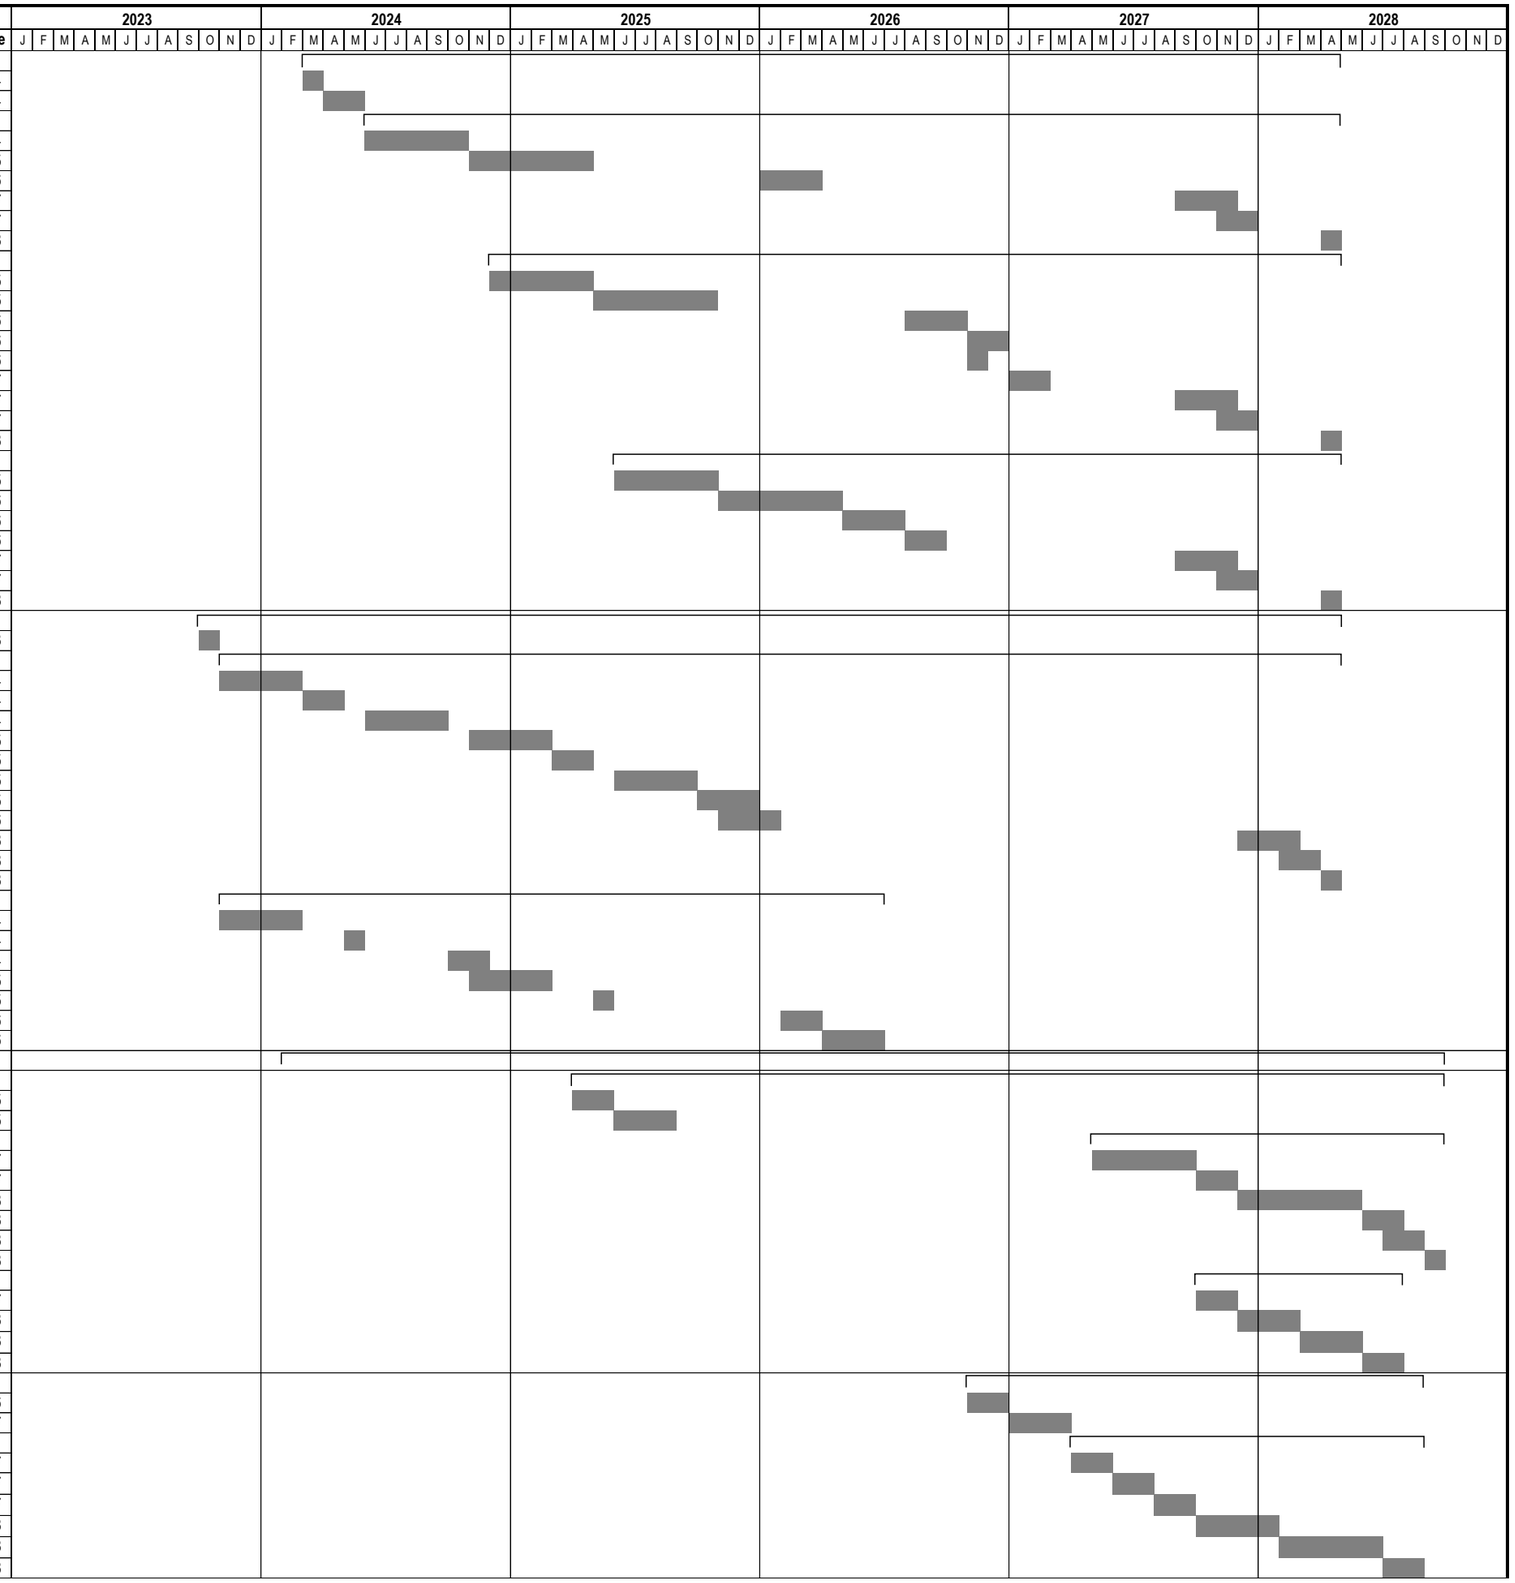

Appendix 2.1 Tentative Construction Programme
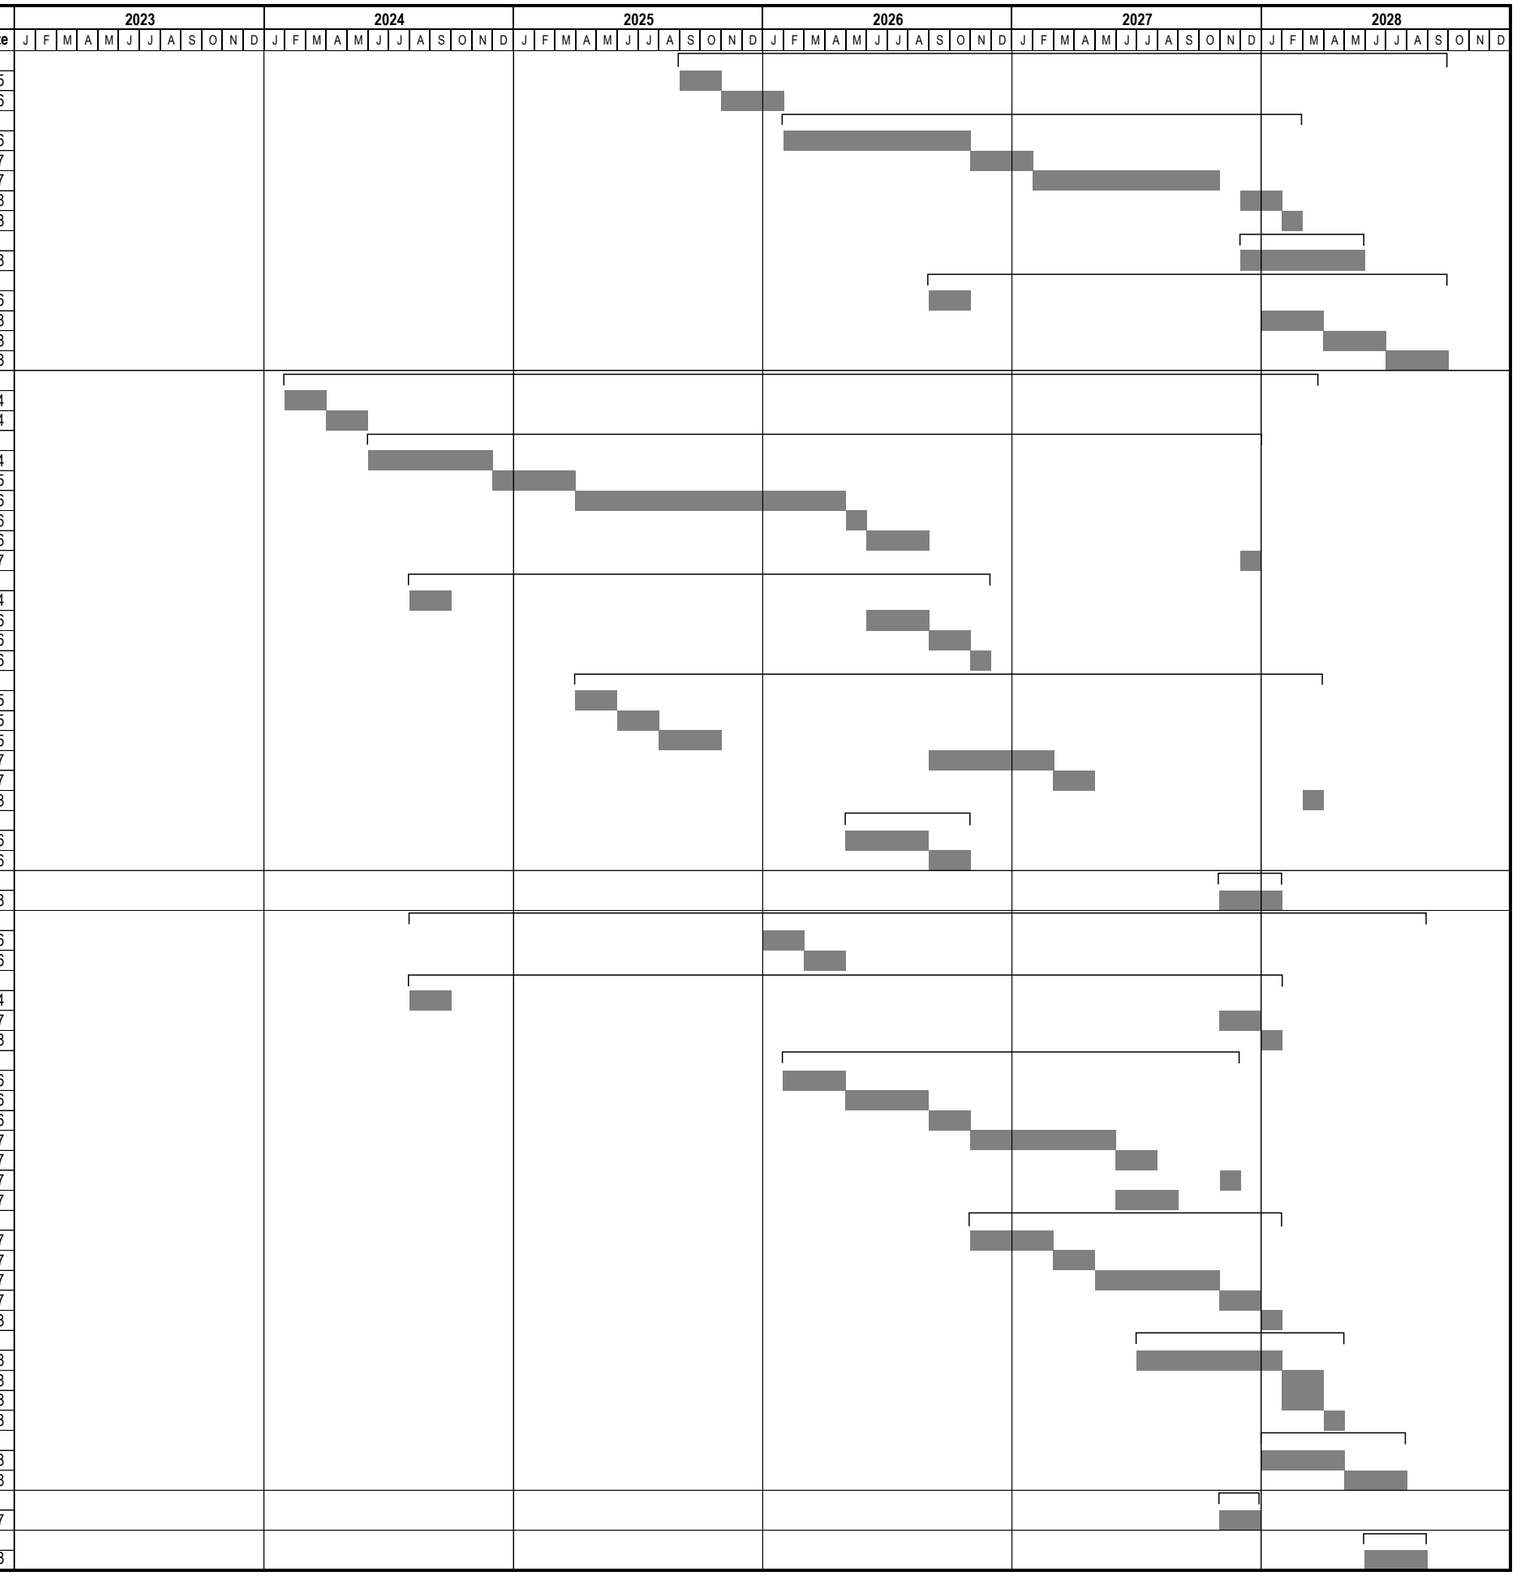
Activity ID	Description	Start Date	End Date
147	**(B2) Work Zone B2**		
148	(B2.1) Site Clearance / Set-up / Plant Mobilization / Tree Felling and Transplanting Works	09-2025	10-2025
149	(B2.2) Utilities Protection and Diversion Works	11-2025	01-2026
150	**(B2.3) Construction of Underpass and Depressed Roads for T4(EB) and T4(WB)**		
151	(B2.3.1) Temporary Works for ELS	02-2026	10-2026
152	(B2.3.2) Excavation	11-2026	01-2027
153	(B2.3.3) Structures for Underpass and Depressed Roads	02-2027	10-2027
154	(B2.3.4) Roadworks, Drainage, E&M Works	12-2027	01-2028
155	(B2.3.5) Pavement	02-2028	02-2028
156	**(B2.4) Reinstatement Works**		
157	(B2.4.1) Roadworks, Drainage & Utilities	12-2027	05-2028
158	**(B2.5) Construction of Footbridge across CKMR**		
159	(B2.5.1) Piling Works	09-2026	10-2026
160	(B2.5.2) Pile Caps and Piers	01-2028	03-2028
161	(B2.5.3) Bridge Deck	04-2028	06-2028
162	(B2.5.4) Associated Structures (Stairs & Lifts)	07-2028	09-2028
163	**(B3) Work Zone B3**		
164	(B3.1) Site Clearance / Set-up / Plant Mobilization / Tree Felling and Transplanting Works	02-2024	03-2024
165	(B3.2) Utilities Protection and Diversion Works	04-2024	05-2024
166	**(B3.3) Construction of Underpass and Depressed Roads for T4(EB) and T4(WB)**		
167	(B3.3.1) Temporary Works for ELS	06-2024	11-2024
168	(B3.3.2) Excavation	12-2024	03-2025
169	(B3.3.3) Structures for Underpass and Depressed Roads	04-2025	04-2026
170	(B3.3.4) Noise Barriers	05-2026	05-2026
171	(B3.3.5) Roadworks, Drainage, E&M Works	06-2026	08-2026
172	(B3.3.6) Pavement	12-2027	12-2027
173	**(B3.4) Modification of Sha Tin Road**		
174	(B3.4.1) Temporary Realignment	08-2024	09-2024
175	(B3.4.2) Permanent Structures supporting Sha Tin Road	06-2026	08-2026
176	(B3.4.3) Roadworks, Drainage & Utilities	09-2026	10-2026
177	(B3.4.4) Pavement	11-2026	11-2026
178	**(B3.5) Construction of T4(EB) Slip Road SR6-1**		
179	(B3.5.1) Temporary Works for ELS	04-2025	05-2025
180	(B3.5.2) Excavation	06-2025	07-2025
181	(B3.5.3) Retaining Structures for At-grade Road	08-2025	10-2025
182	(B3.5.4) Retaining Structures for At-grade Road on top of Underpass	09-2026	02-2027
183	(B3.5.5) Roadworks, Drainage & Utilities	03-2027	04-2027
184	(B3.5.6) Pavement	03-2028	03-2028
185	**(B3.6) Reinstatement Works**		
186	(B3.6.1) Slopework	05-2026	08-2026
187	(B3.6.2) Roadworks, Drainage & Utilities	09-2026	10-2026
188	**(B3a) Work Zone B3a**		
189	(B3a.1) Slopework	11-2027	01-2028
190	**(B4) Work Zone B4**		
191	(B4.1) Site Clearance / Set-up / Plant Mobilization / Tree Felling and Transplanting Works	01-2026	02-2026
192	(B4.2) Utilities Protection and Diversion Works	03-2026	04-2026
193	**(B4.3) Modification of Sha Tin Road**		
194	(B4.3.1) Temporary Realignment	08-2024	09-2024
195	(B4.3.2) Roadworks, Drainage & Utilities	11-2027	12-2027
196	(B4.3.3) Pavement	01-2028	01-2028
197	**(B4.4) Construction of Depressed Roads for T4(EB)**		
198	(B4.4.1) Removal of Existing Noise Barrier along Sha Tin Road	02-2026	04-2026
199	(B4.4.2) Temporary Works for ELS	05-2026	08-2026
200	(B4.4.3) Excavation	09-2026	10-2026
201	(B4.4.4) Structures for Depressed Roads	11-2026	05-2027
202	(B4.4.5) Roadworks, Drainage, E&M Works	06-2027	07-2027
203	(B4.4.6) Pavement	11-2027	11-2027
204	(B4.4.7) Reinstatement of Slope	06-2027	08-2027
205	**(B4.5) Construction of Depressed Roads for T4(WB)**		
206	(B4.5.1) Temporary Works for ELS	11-2026	02-2027
207	(B4.5.2) Excavation	03-2027	04-2027
208	(B4.5.3) Structures for Depressed Roads	05-2027	10-2027
209	(B4.5.4) Roadworks, Drainage, E&M Works	11-2027	12-2027
210	(B4.5.5) Pavement	01-2028	01-2028
211	**(B4.6) Construction of T4(EB) Slip Road SR6-1**		
212	(B4.6.1) Retaining Structures for At-grade Road	07-2027	01-2028
213	(B4.6.2) Slopework	02-2028	03-2028
214	(B4.6.3) Roadworks, Drainage & Utilities	02-2028	03-2028
215	(B4.6.4) Pavement	04-2028	04-2028
216	**(B4.7) Noise Barriers / Enclosures**		
217	(B4.7.1) Frame	01-2028	04-2028
218	(B4.7.2) Panel	05-2028	07-2028
219	**(B4a) Work Zone B4a**		
220	(B4a.1) Slopework	11-2027	12-2027
221	**(B5) Work Zone B5**		
222	(B5.1) Roadworks & Pavement	06-2028	08-2028
