Figure 17.2 Programme for Implementation of Lamma South Island Landfill (LSIL)
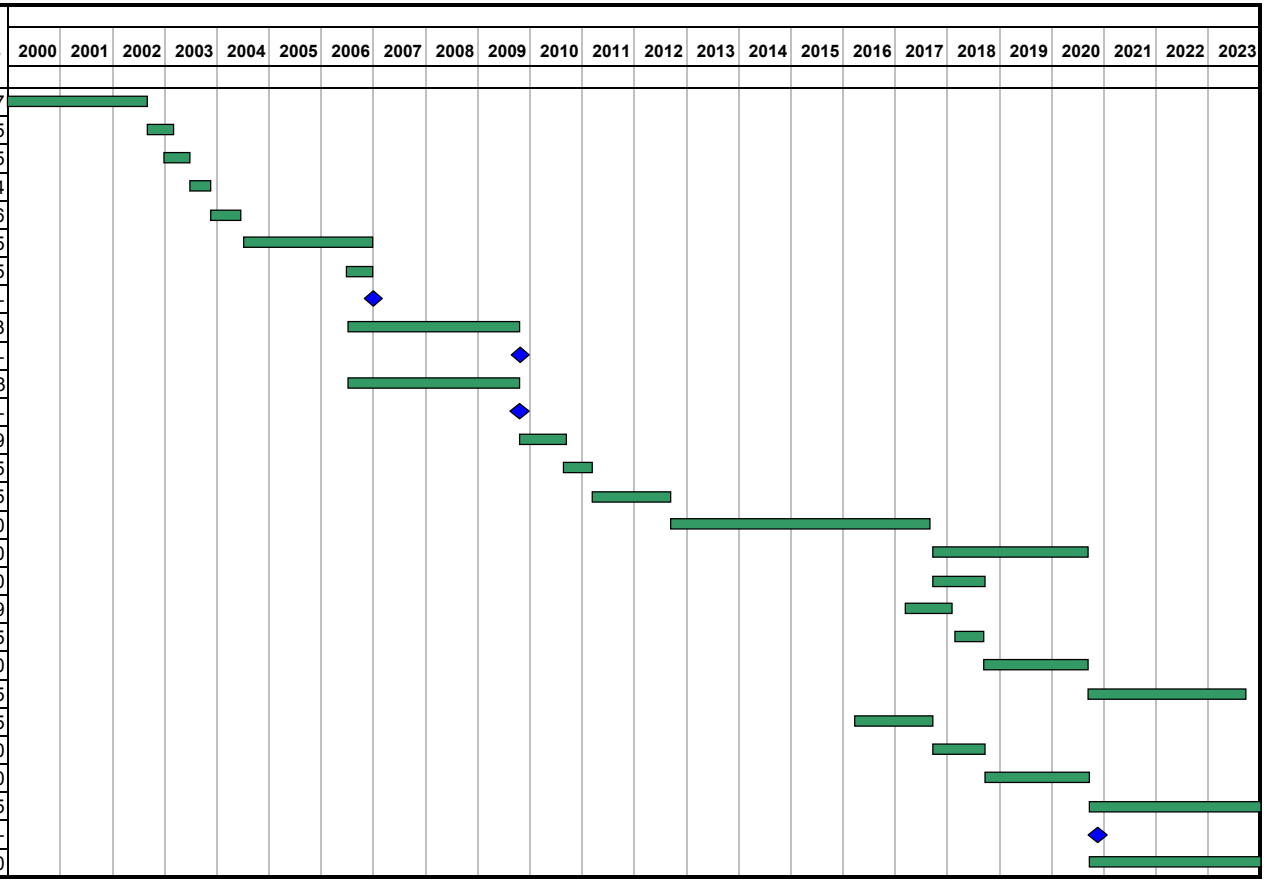
Description	Years
Extension of Existing Landfills etc Study (CE 45/99)	2.7
Consultation	0.5
Creating Cat. C Project	0.5
Upgrading to Cat. B Project	0.4
Consultants Selection	0.6
Lamma South Island Landfill Feasibility Study (TIA, EIA, etc)	2.5
Environmental Impact Assessment Ordinance (EIAO) Procedures	0.5
Environmental Permit Issued	-
Town Planning Ordinance Procedures	3.3
EXCO Approval	-
Foreshore & Sea-bed (Reclamations) Ordinance	3.3
EXCO Approval	-
Preparation of Tender Documents for Cell 1 Seawall & Reclamation	0.9
Tendering Cell 1 Seawall & Reclamation	0.5
Cell 1 Dredging and Seawall	1.5
Cell 1 Filling behind Seawall (50 ha.)	5.0
Cell 1 Filling behind Seawall (Remainder)	3.0
Cell 1 Settlement Period for first 50 ha.	1.0
Preparation of Tender Documents for Cell 2 Seawall & Reclamation	0.9
Tendering Cell 2 Seawall & Reclamation	0.5
Cell 2 Dredging and Seawall	2.0
Cell 2 Filling behind Seawall	9.5
Preparation of Tender Documents for Landfill Contract	1.5
Tendering Landfill Contract	1.0
Initial Development Phase to Achieve Operation	2.0
Subsequent Development Phases for Landfill	11.5
Landfill Operation Starts	-
Landfill Operation	13.0
