TUEN MUN-CHEK LAP KOK LINK
PRELIMINARY CONSTRUCTION PROGRAMME

ACTIVITIES		
NORTHERN SECTION		
NORTHERN RECLAMATION	N-C	PLANT MOBILIZATION
		DREDGING FOR SEAWALL AND RECLAMATION
		FILLING FOR SEAWALL(ROCK FILL/PUBLIC FILL)
		CONSTRUCTION SEAWALL
		PUBLIC FILL FOR RECLAMATION
	N-A AND N-B	DREDGING FOR SEAWALL
		FILLING FOR SEAWALL(ROCK FILL/PUBLIC FILL)
		CONSTRUCTION SEAWALL
		PUBLIC FILL FOR RECLAMATION
VIADUCT CONNECTION & SLIP ROADS	AREA A	SUB-STRUCTURE
		DECK ERECTION
		STREET FURNITURE, PAVEMENT, FITTING OUT
	AREA C	SUB-STRUCTURE
		DECK ERECTION
		STREET FURNITURE, PAVEMENT, FITTING OUT
	AREA E	SUB-STRUCTURE
		DECK ERECTION
		STREET FURNITURE, PAVEMENT, FITTING OUT
	AREA G	SUB-STRUCTURE
		DECK ERECTION
		STREET FURNITURE, PAVEMENT, FITTING OUT
	AREA J	SUB-STRUCTURE
		DECK ERECTION
		STREET FURNITURE, PAVEMENT, FITTING OUT
	AREA K	SUB-STRUCTURE
		DECK ERECTION
		STREET FURNITURE, PAVEMENT, FITTING OUT
TOLL PLAZA	AREA A	EARTH WORKS
		SLOPE WORKS
		UTILITIES INSTALLATION
		ROAD WORKS
		STREET FURNITURE, PAVEMENT, FITTING OUT
	AREA B	EARTH WORKS
		SLOPE WORKS
		UTILITIES INSTALLATION
		ROAD WORKS
		STREET FURNITURE, PAVEMENT, FITTING OUT
	AREA C	RETAINING WALL
	AREA D	EARTH WORKS
		SLOPE WORKS
		UTILITIES INSTALLATION
		ROAD WORKS
		STREET FURNITURE, PAVEMENT, FITTING OUT
	ADMIN BLDG.	FOUNDATION
		SUPERSTRUCTURE
		ARCHITECTURAL FINISHES AND BUILDING SERVICES
	AREA E	EARTH WORKS
		SLOPE WORKS
		UTILITIES INSTALLATION
		ROAD WORKS
		STREET FURNITURE, PAVEMENT, FITTING OUT
	AREA F	UNDERGROUND UTILITIES INSTALLATION
		ROAD FINISHES
		E&M INSTALLATION
	AREA G	UNDERGROUND UTILITIES INSTALLATION
		ROAD FINISHES
		E&M INSTALLATION
	AREA H	UNDERGROUND UTILITIES INSTALLATION
		ROAD FINISHES
		E&M INSTALLATION
	AREA I	UNDERGROUND UTILITIES INSTALLATION
		ROAD FINISHES
		E&M INSTALLATION

YEAR 2010: A S O N D
YEAR 2011: J F M A M J J A S O N D
YEAR 2012: J F M A M J J A S O N D
YEAR 2013: J F M A M J J A S O N D
YEAR 2014: J F M A M J J A S O N D
YEAR 2015: J F M A M J J A S O N D
YEAR 2016: J F M A M J J A S O N D
YEAR 2017: J F M A M J J A S

MAUNSELL | AECOM
Maunsell Consultants Asia Ltd

AGREEMENT NO. CE 52/2007(HY)
TUEN MUN - CHEK LAP KOK LINK - INVESTIGATION

INDICATIVE CONSTRUCTION PROGRAMME IN TUEN MUN

SCALE	--	DATE	MAY 2009
CHECK	--	DRAWN	ZKG
JOB No.	60044963	DRAWING No.	FIGURE 3.9a
		REV	--

Plotting By: 08/05/2009 tseyme
PLOT SCALE: 1=120.375

C:\Documents and Settings\tseyme\Desktop\FIGURE 3.9a.dgn

TUEN MUN-CHEK LAP KOK LINK
PRELIMINARY CONSTRUCTION PROGRAMME

ACTIVITIES		
TUNNEL	TUNNEL	TBM MOBILIATION
		EXCAVATION FOR TUNNEL LAUNCHING PIT
		TUNNEL BORING(1ST)
		TUNNEL BORING(2ND)
		E&M AND FITTING OUT
SOUTHERN SECTION		
SOUTHERN RACLCAMATION	S-A	PLANT MOBILIZATION
		DREDGING FOR SEAWALL AND RECLAMATION
		FILLING FOR SEAWALL
		CONSTRUCTION SEAWALL
		FILLING FOR RECLAMATION
	S-B	DREDGING FOR SEAWALL
		FILLING FOR SEAWALL(ROCK FILL/PUBLIC FILL)
		CONSTRUCTION SEAWALL
		FILLING FOR RECLAMATION
	S-C	DREDGING FOR SEAWALL
		FILLING FOR SEAWALL(ROCK FILL/PUBLIC FILL)
		CONSTRUCTION SEAWALL
		FILLING FOR RECLAMATION
VIADUCT CONNECTION & SLIP ROADS	AREA A	SLOPE WORKS
		DIVERSION UTILITIES
		CHEUNG TUNG ROAD DIVERSION
		SUB-STRUCTURE
		DECK ERECTION
		STREET FURNITURE, PAVEMENT, FITTING OUT
	AREA B	SUB-STRUCTURE
		DECK ERECTION
		STREET FURNITURE, PAVEMENT, FITTING OUT
	AREA C	SUB-STRUCTURE
		DECK ERECTION
		STREET FURNITURE, PAVEMENT, FITTING OUT
	AREA D	SUB-STRUCTURE
		DECK ERECTION
		STREET FURNITURE, PAVEMENT, FITTING OUT
	AREA E	SUB-STRUCTURE
		DECK ERECTION
		STREET FURNITURE, PAVEMENT, FITTING OUT
	AREA F	SUB-STRUCTURE
		DECK ERECTION
		STREET FURNITURE, PAVEMENT, FITTING OUT
	AREA G	SUB-STRUCTURE
		DECK ERECTION
		STREET FURNITURE, PAVEMENT, FITTING OUT
	AREA H	SUB-STRUCTURE
		DECK ERECTION
		STREET FURNITURE, PAVEMENT, FITTING OUT
	AREA I	UTILITIES DIVERSION
		CHEUNG TUNG ROAD DIVERSION
		SUB-STRUCTURE
		DECK ERECTION
		STREET FURNITURE, PAVEMENT, FITTING OUT

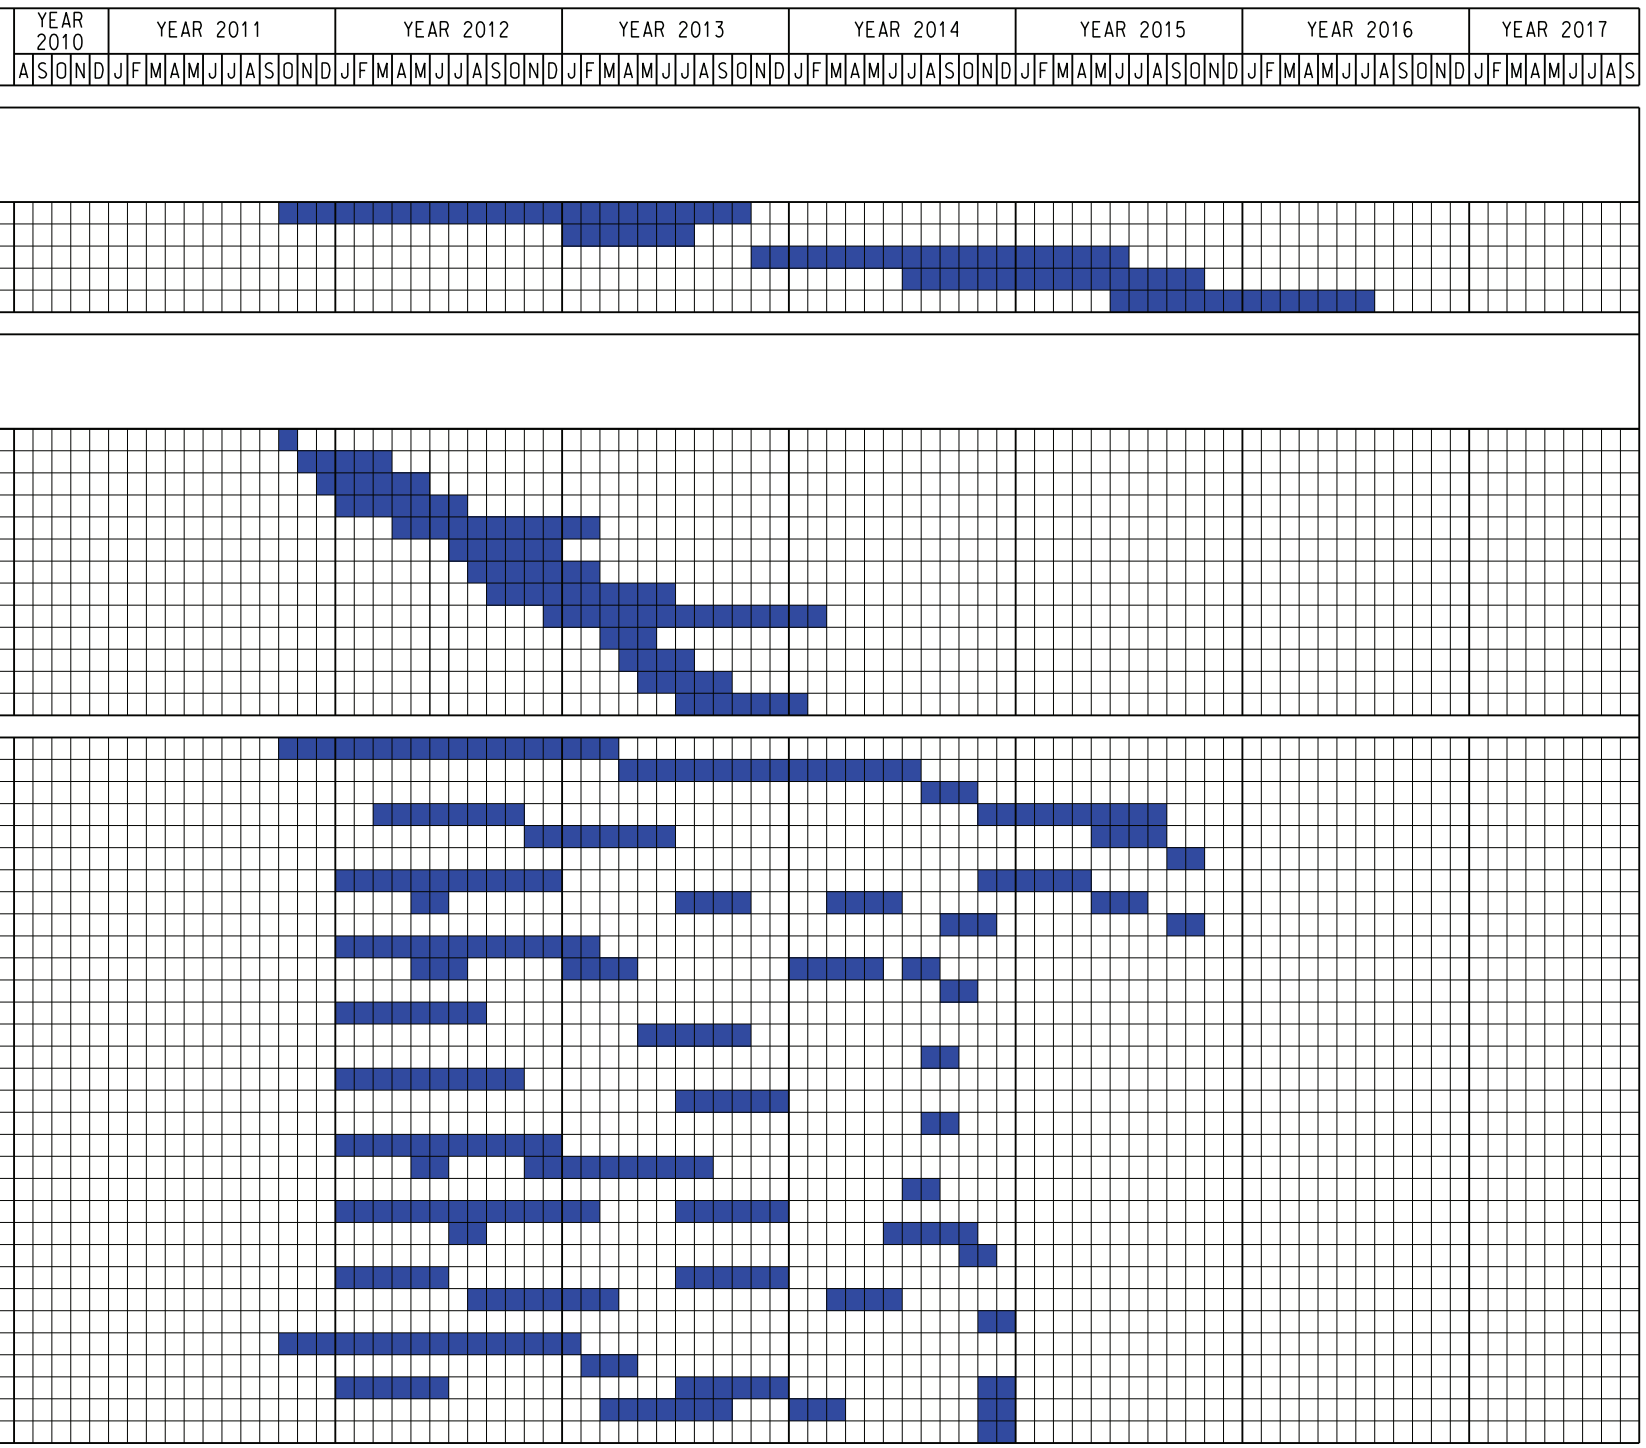

MAUNSELL | AECOM
Maunsell Consultants Asia Ltd

AGREEMENT NO. CE 52/2007(HY)
TUEN MUN - CHEK LAP KOK LINK - INVESTIGATION

INDICATIVE CONSTRUCTION PROGRAMME IN NORTH LANTAU

SCALE	--	DATE	MAY 2009
CHECK	--	DRAWN	ZKG
JOB No.	60044963	DRAWING No.	FIGURE 3.9b
		REV	--

Plotting By huy 2009-5-7
PLOT SCALE 1:20

p:\PROJECTS\60044963\DRAWING\FIGURE\EIA REPORT\FIGURE 3 9b dgn
