Appendix 2.2 - Tentative Construction Programme

Improvement of Lion Rock Tunnel

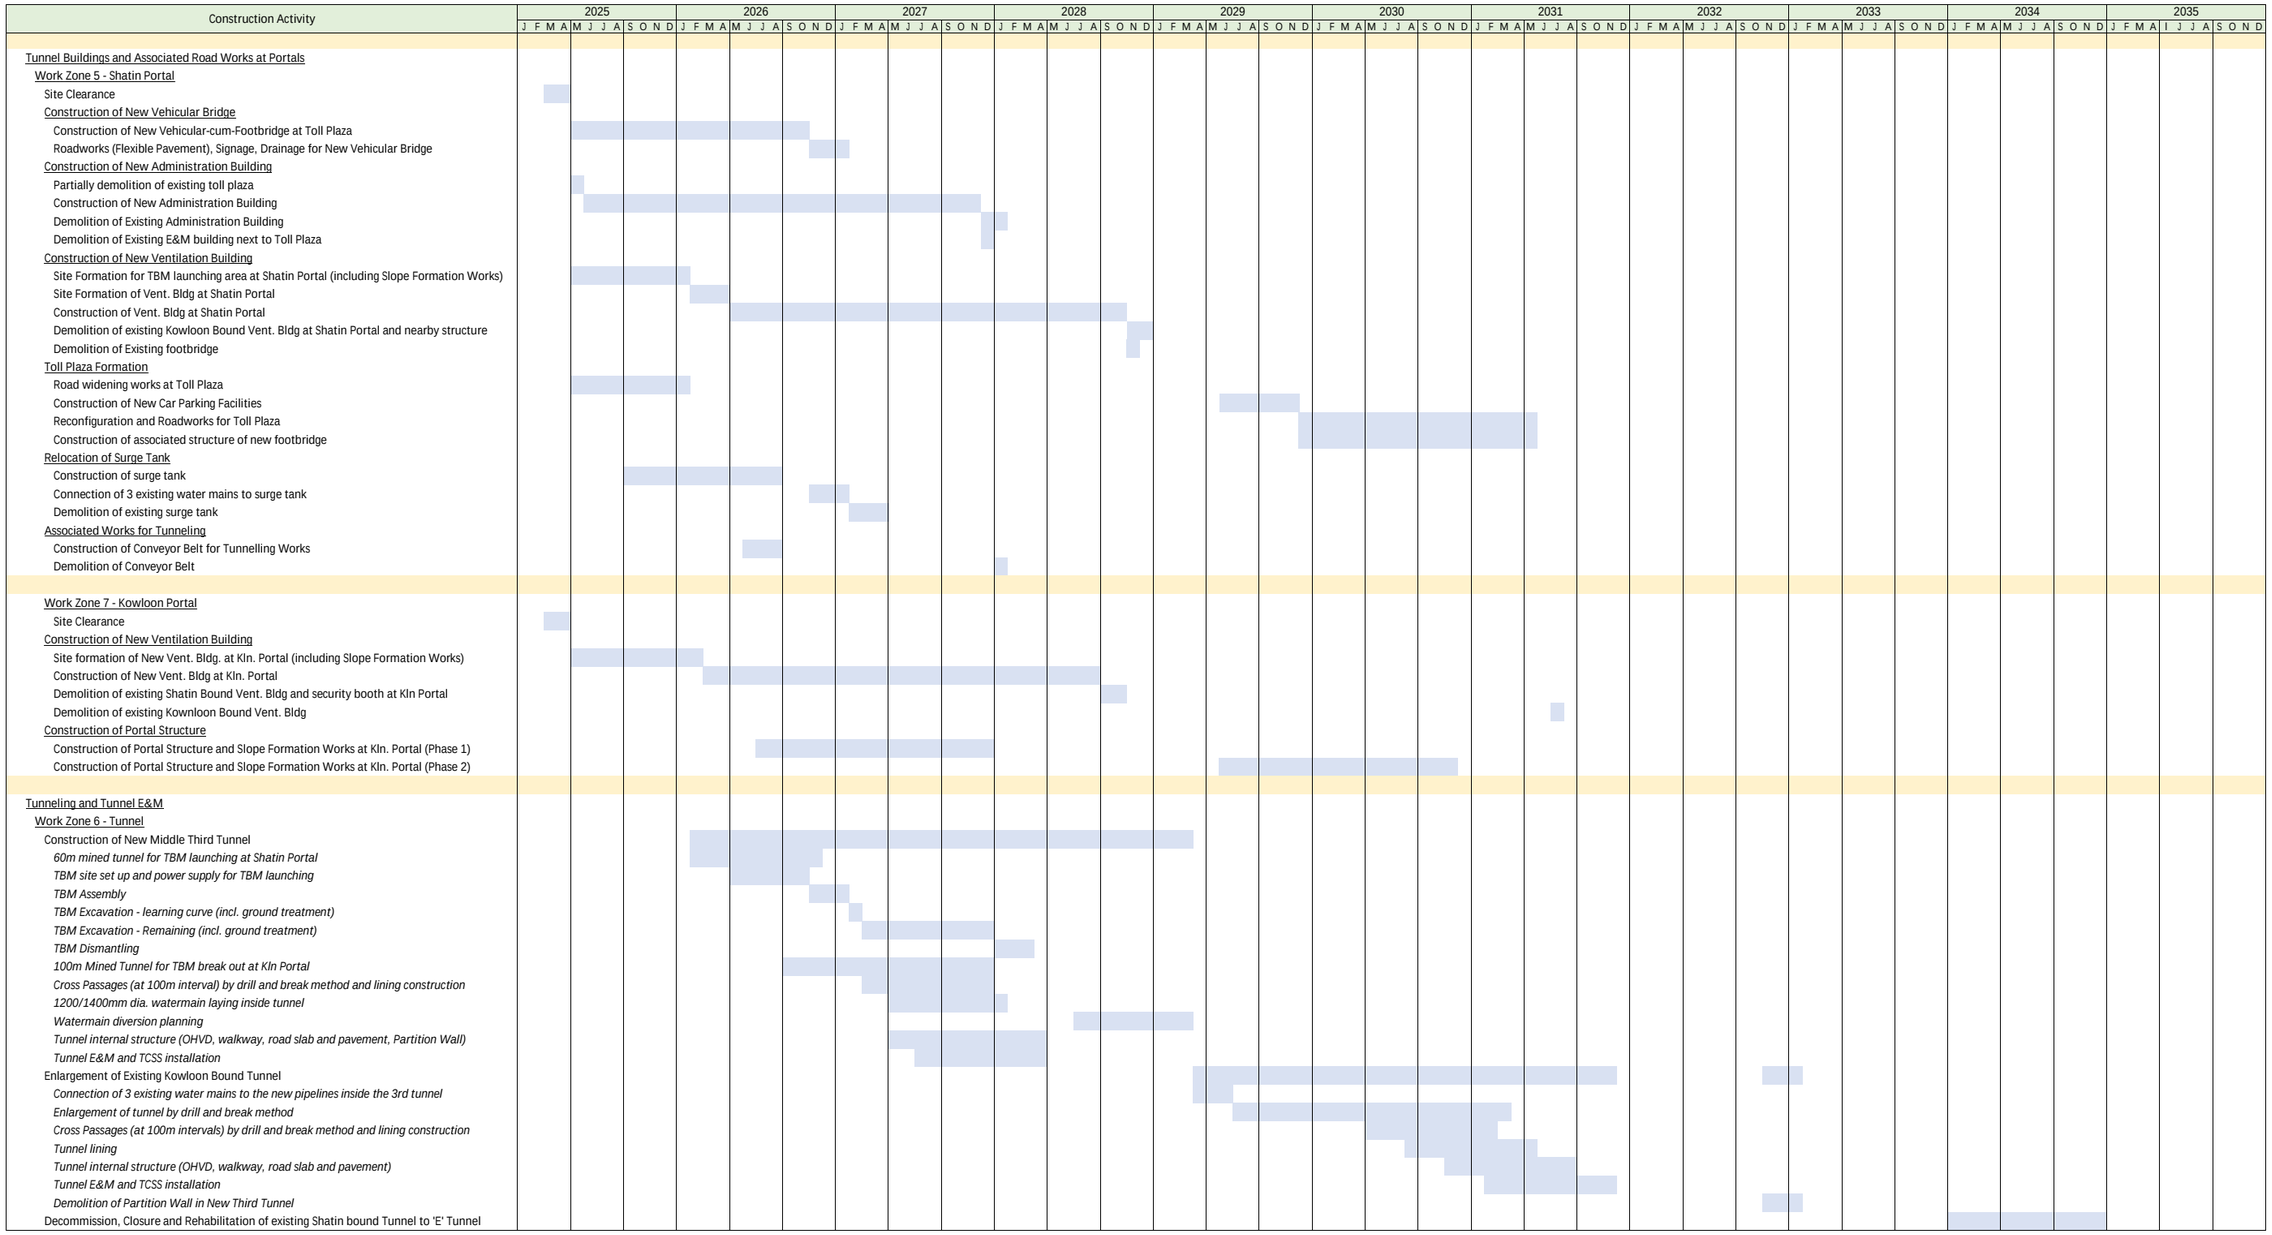

Appendix 2.2 - Tentative Construction Programme

Appendix 2.2 - Tentative Construction Programme

Construction Activity	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035
	J F M A M J J A S O N D	J F M A M J J A S O N D	J F M A M J J A S O N D	J F M A M J J A S O N D	J F M A M J J A S O N D	J F M A M J J A S O N D	J F M A M J J A S O N D	J F M A M J J A S O N D	J F M A M J J A S O N D	J F M A M J J A S O N D	J F M A I J J A S O N D
Work Zone 3											
Preparatory works											
Site Clearance and Tree felling / transplant											
Road Widening and Installtion of Noise Barrier											
Widening works at north bound (including slip road)											
Slope Formation / Upgrading Works											
Foundation of Noise Barrier											
Pile Cap, L-retaining Wall and Formation of new road											
Utilities Diversion											
Erection of structural steel post for noise barrier											
Widening works at central divider											
Foundation of Noise Barrier											
Pile Cap and Footing											
Erection of structural steel post for noise barrier											
Widening works at south bound											
Slope Formation / Upgrading Works											
Foundation of Noise Barrier											
Pile Cap and Formation of new road											
Utilities Diversion											
Erection of structural steel post for noise barrier											
Installation of steel member and noise barrier panel											
Erection of steel member and noise barrier panel at north bound											
Erection of steel member and noise barrier panel at south bound											
Roadworks											
Roadworks at north bound											
Road Drainage											
Road Surfacing											
Roadlighting and E&M works											
Roadworks at south bound											
Road Drainage											
Road Surfacing											
Roadlighting and E&M works											
Landscaping Works											
Landscaping works at north bound											
Landscaping works at south bound											
Work Zone 4											
Preparatory works											
Site Clearance and Tree felling / transplant											
Road Widening and Installtion of Noise Barrier											
Widening works at north bound											
Slope Formation / Upgrading Works											
Foundation of Noise Barrier											
Pile Cap, L-retaining Wall and Formation of new road											
Utilities Diversion											
Erection of structural steel post for noise barrier											
Widening works at central divider											
Foundation of Noise Barrier											
Pile Cap and Footing											
Erection of structural steel post for noise barrier											
Widening works at south bound											
Slope Formation / Upgrading Works											
Foundation of Noise Barrier											
Formation of new road											
Utilities Diversion											
Erection of structural steel post for noise barrier											
Installation of steel member and noise barrier panel											
Erection of steel member and noise barrier panel at north bound											
Erection of steel member and noise barrier panel at south bound											
Roadworks											
Roadworks at north bound											
Road Drainage											
Road Surfacing											
Roadlighting and E&M works											
Roadworks at south bound											
Road Drainage											
Road Surfacing											
Roadlighting and E&M works											
Landscaping Works											
Landscaping works at north bound											
