Figure 16.2 Programme for Implementation of Lamma North Island Landfill (LNIL)
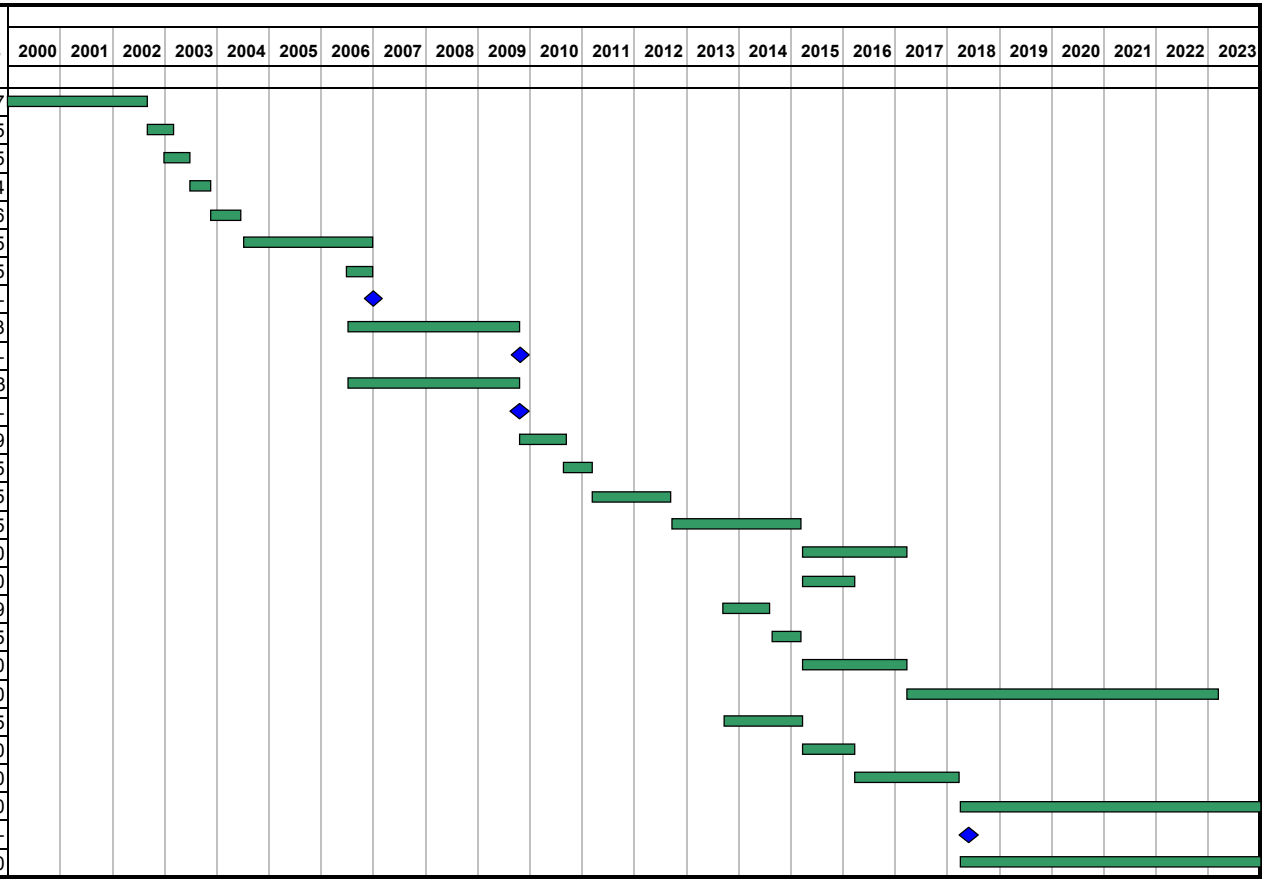
Description	Years
Extension of Existing Landfills etc Study (CE 45/99)	2.7
Consultation	0.5
Creating Cat. C Project	0.5
Upgrading to Cat. B Project	0.4
Consultants Selection	0.6
Lamma North Island Landfill Feasibility Study (TIA, EIA, etc)	2.5
Environmental Impact Assessment Ordinance (EIAO) Procedures	0.5
Environmental Permit Issued	-
Town Planning Ordinance Procedures	3.3
EXCO Approval	-
Foreshore & Sea-bed (Reclamations) Ordinance	3.3
EXCO Approval	-
Preparation of Tender Documents for Cell 1 Seawall & Reclamation	0.9
Tendering Cell 1 Seawall & Reclamation	0.5
Cell 1 Seawall Construction	1.5
Cell 1 Filling behind Seawall (50 ha.)	2.5
Cell 1 Filling behind Seawall (Remainder)	2.0
Cell 1 Settlement Period for first 50 ha.	1.0
Preparation of Tender Documents for Cell 2 Seawall & Reclamation	0.9
Tendering Cell 2 Seawall & Reclamation	0.5
Cell 2 Seawall Construction	2.0
Cell 2 Filling behind Seawall	6.0
Preparation of Tender Documents for Landfill Contract	1.5
Tendering Landfill Contract	1.0
Initial Development Phase to Achieve Operation	2.0
Subsequent Development Phases for Landfill	7.0
Landfill Operation Starts	-
Landfill Operation	17.0
