Tentative Programme for HKLR

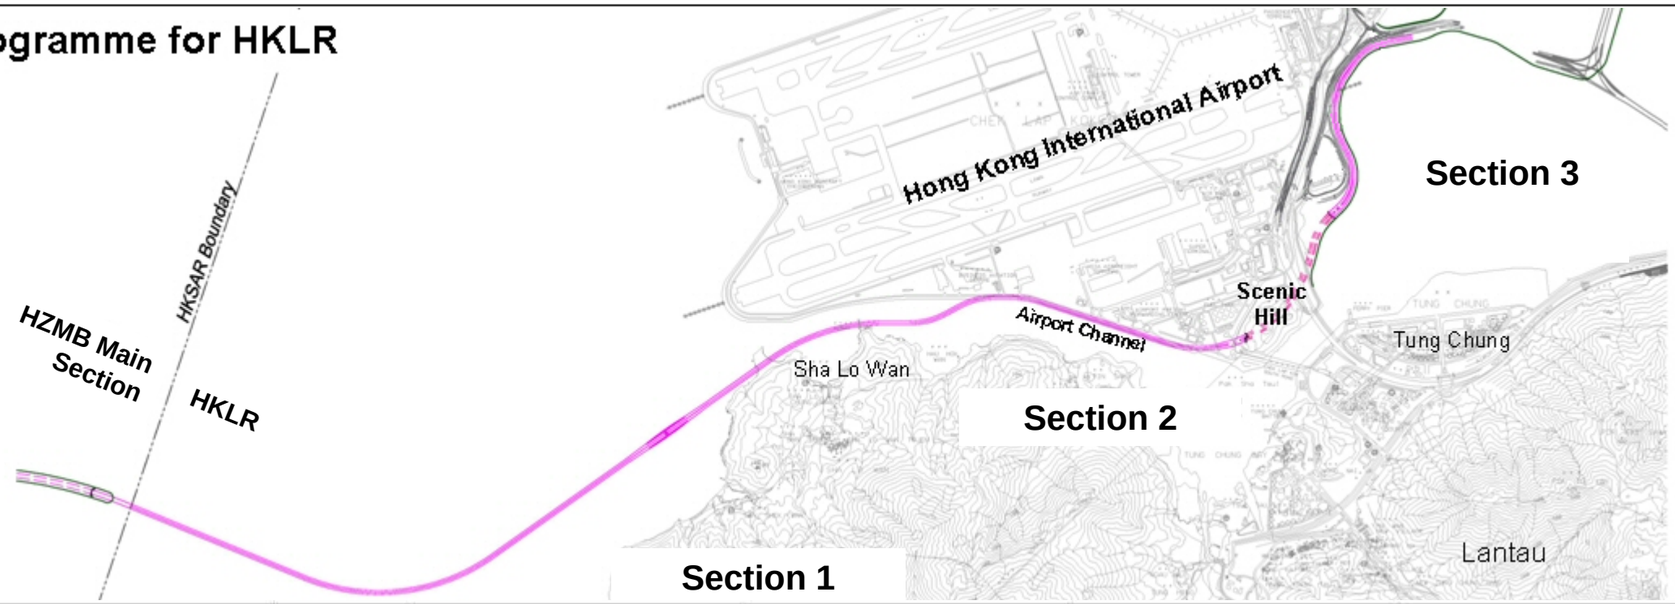

Activities		Year 2010					Year 2011										Year 2012										Year 2013										Year 2014										Year 2015					
		A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J
Section 1	Design + GI works																																																				
	Pile foundation + pile cap																																																				
	Superstructure of viaduct																																																				
Section 2	Design + GI works																																																				
	Pile foundation + pile cap																																																				
	Superstructure of viaduct																																																				
Section 3	Design + GI works																																																				
	Dredging for seawall (Portion 1)																																																				
	Filling for seawall (Portion 1)																																																				
	Dredging for Reclamation (Portion 1)																																																			
	Geotextile (Portion 1)																																																				
	Installation of band drains (Portion 1)																																																				
	Filling for Reclamation (Sandfill - Portion 1)																																																			
	Filling for reclamation (Public fill - Portion 1)																																																			
	Surcharge (Fully-dredged area in Portion 1)																																																			
	Surcharge (Non-dredged area in Portion 1)																																																			
	Dredging for seawall & reclamation (Portions 2 & 3)																																																			
	Filling for seawall & reclamation (Portions 2 & 3)																																																			
	Filling for reclamation (Public fill - Portions 2 & 3)																																																			
	Surcharge (Portions 2 & 3)																																																			
	Tunnel construction (land portion)																																																			
	Tunnel construction (reclamation portion)																																																			
	Construction of at-grade road																																																			

路政署 HIGHWAYS DEPARTMENT
港珠澳大橋香港工程管理處
Hong Kong - Zhuhai - Macao Bridge
Hong Kong Project Management Office

ARUP
奧雅納工程顧問
Ove Arup & Partners
Hong Kong Limited

Drawing Title

Tentative Programme for HKLR

Drawing No.

Figure 4.14
