Appendix 2.1c Tentative Construction Programme (Reprovisioning Option C)

ID	Task Name	Duration	Start	Finish
1	**Stage 1_Scenario 4.5yr**	**1643 day**	**Tue 1/9/15**	**Sat 29/2/20**
2	Commencement	0 days	Tue 1/9/15	Tue 1/9/15
3	Preliminary	153 days	Tue 1/9/15	Sun 31/1/16
4	Stage I Excavation (For Zone 1A & 3)	275 days	Tue 1/12/15	Wed 31/8/16
5	Backfill soil to Zone 1A & 3	91 days	Fri 1/4/16	Thu 30/6/16
6	Import Fill to Zone 1A & 3	61 days	Fri 1/4/16	Tue 31/5/16
7	Stage II Excavation (For Zone 2)	306 days	Fri 1/4/16	Tue 31/1/17
8	Backfill soil to Zone 2	151 days	Sun 1/1/17	Wed 31/5/17
9	Stage III Excavation (For Zone 1B & 1C)	334 days	Mon 1/8/16	Fri 30/6/17
10	Stage IV Excavation (For Zone 4)	184 days	Sat 1/7/17	Sun 31/12/17
11	Stage V Excavation (For Zone 5A & 5B)	274 days	Sat 1/7/17	Sat 31/3/18
12	Foundation for Biopile A at Zone 1A & 3	62 days	Fri 1/7/16	Wed 31/8/16
13	Formation of Biopile A at Zone 1A & 3 (For Zone 1A, 2 & 3)	212 days	Thu 1/9/16	Fri 31/3/17
14	Operation of Biopile A at Zone 1A & 3 (For Zone 1A, 2 & 3)	306 days	Sat 1/4/17	Wed 31/1/18
15	Decomissioning of Biopile A	59 days	Thu 1/2/18	Sat 31/3/18
16	Formation of Biopile B at Zone 1A & 3 (For Zone 1B & 1C)	214 days	Sun 1/4/18	Wed 31/10/18
17	Operation of Biopile B at Zone 1A & 3 (For Zone 1B & 1C)	304 days	Thu 1/11/18	Sat 31/8/19
18	Decomissioning of Biopile B	91 days	Sun 1/9/19	Sat 30/11/19
19	Foundation for Biopile C at Zone 2	61 days	Thu 1/6/17	Mon 31/7/17
20	Formation of Biopile C at Zone 2 (For Zone 4 ,5A & 5B)	212 days	Thu 1/2/18	Fri 31/8/18
21	Operation of Biopile C at Zone 2 (For Zone 4 ,5A & 5B)	303 days	Sat 1/9/18	Sun 30/6/19
22	Decomission of Biopile C	62 days	Mon 1/7/19	Sat 31/8/19
23	Backfill soil to Zone 1B, 1C, 4, 5A & 5B	92 days	Mon 1/7/19	Mon 30/9/19
24	Reinstatement and remaining works	91 days	Sun 1/12/19	Sat 29/2/20
25				
26				
27				

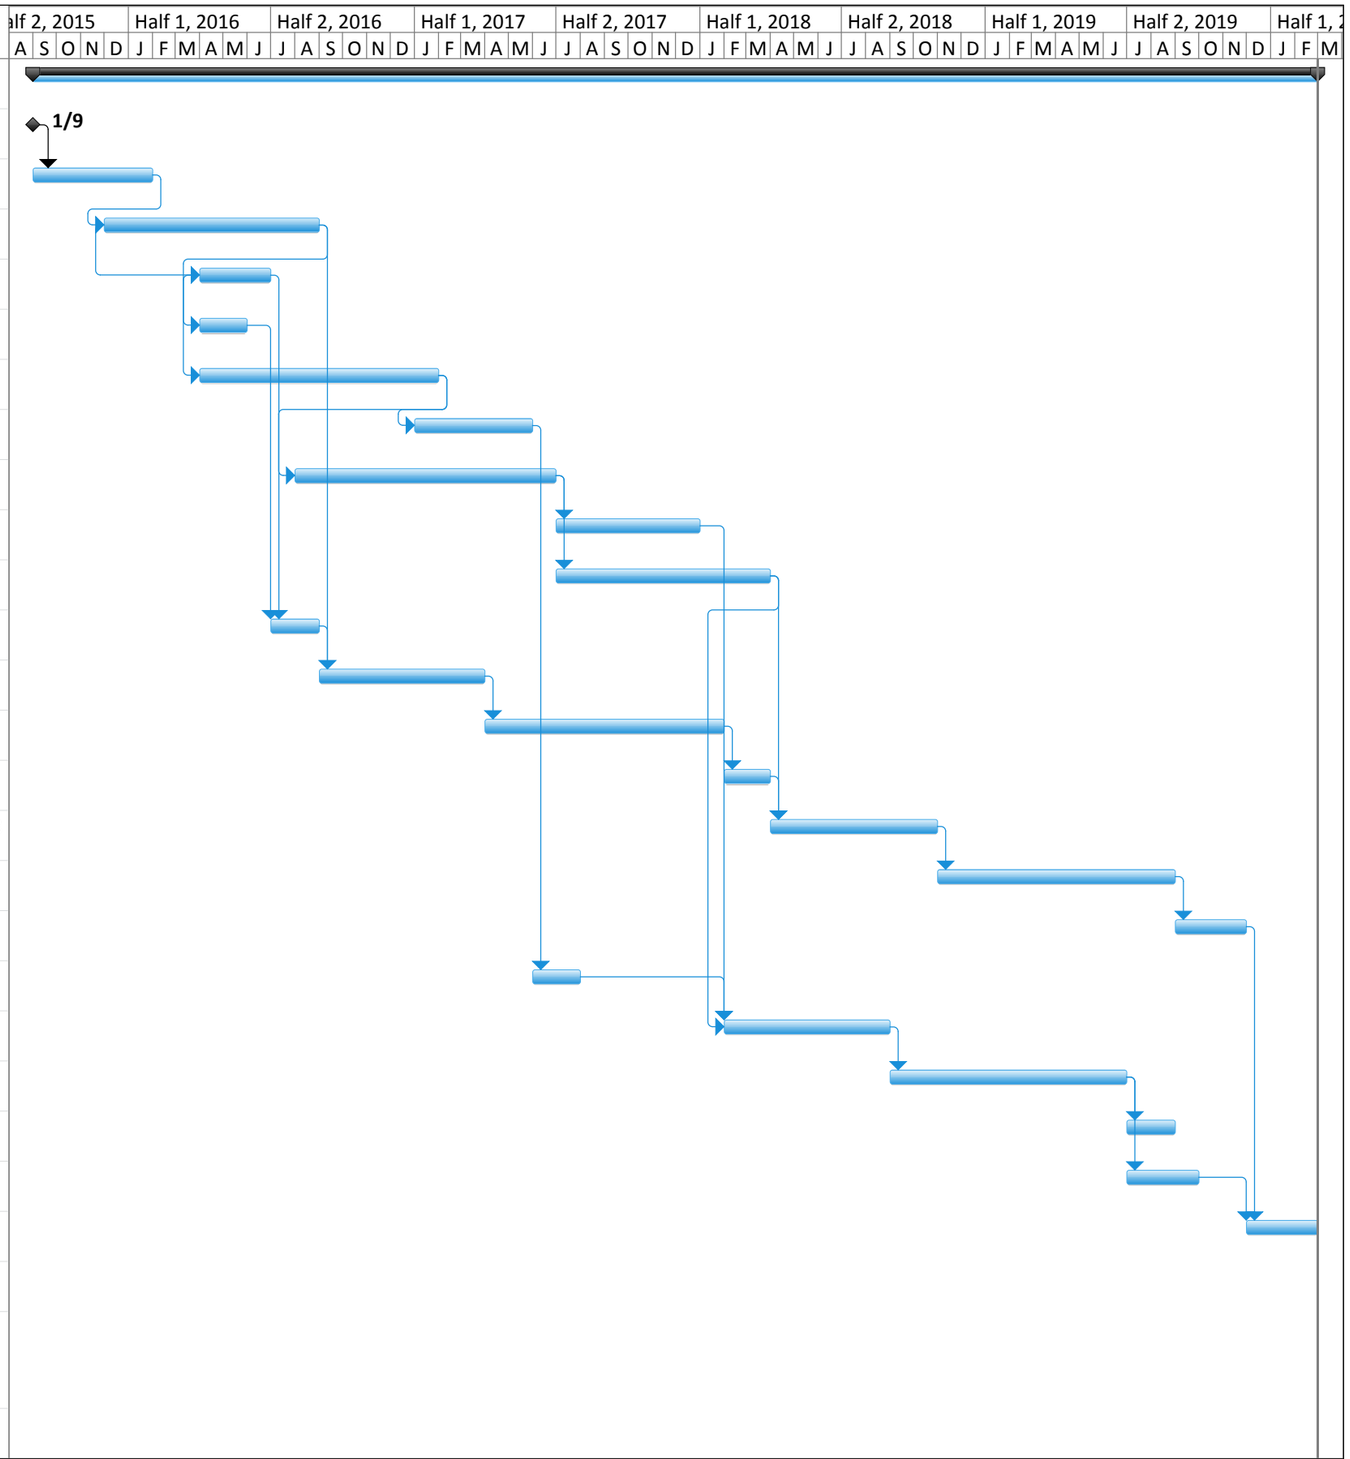

Project: KTCDA_SC_4.5
Date: Wed 30/4/14

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

F:\Leo Pang\203204 KTCDA\Working\Excavation Scheme\Leo_Working\Programme\001_Scheme01_4.5_V6_CEDD.mpp
