APPENDIX 1.1
TENTATIVE CONSTRUCTION PROGRAMME

Tentative Construction Programme
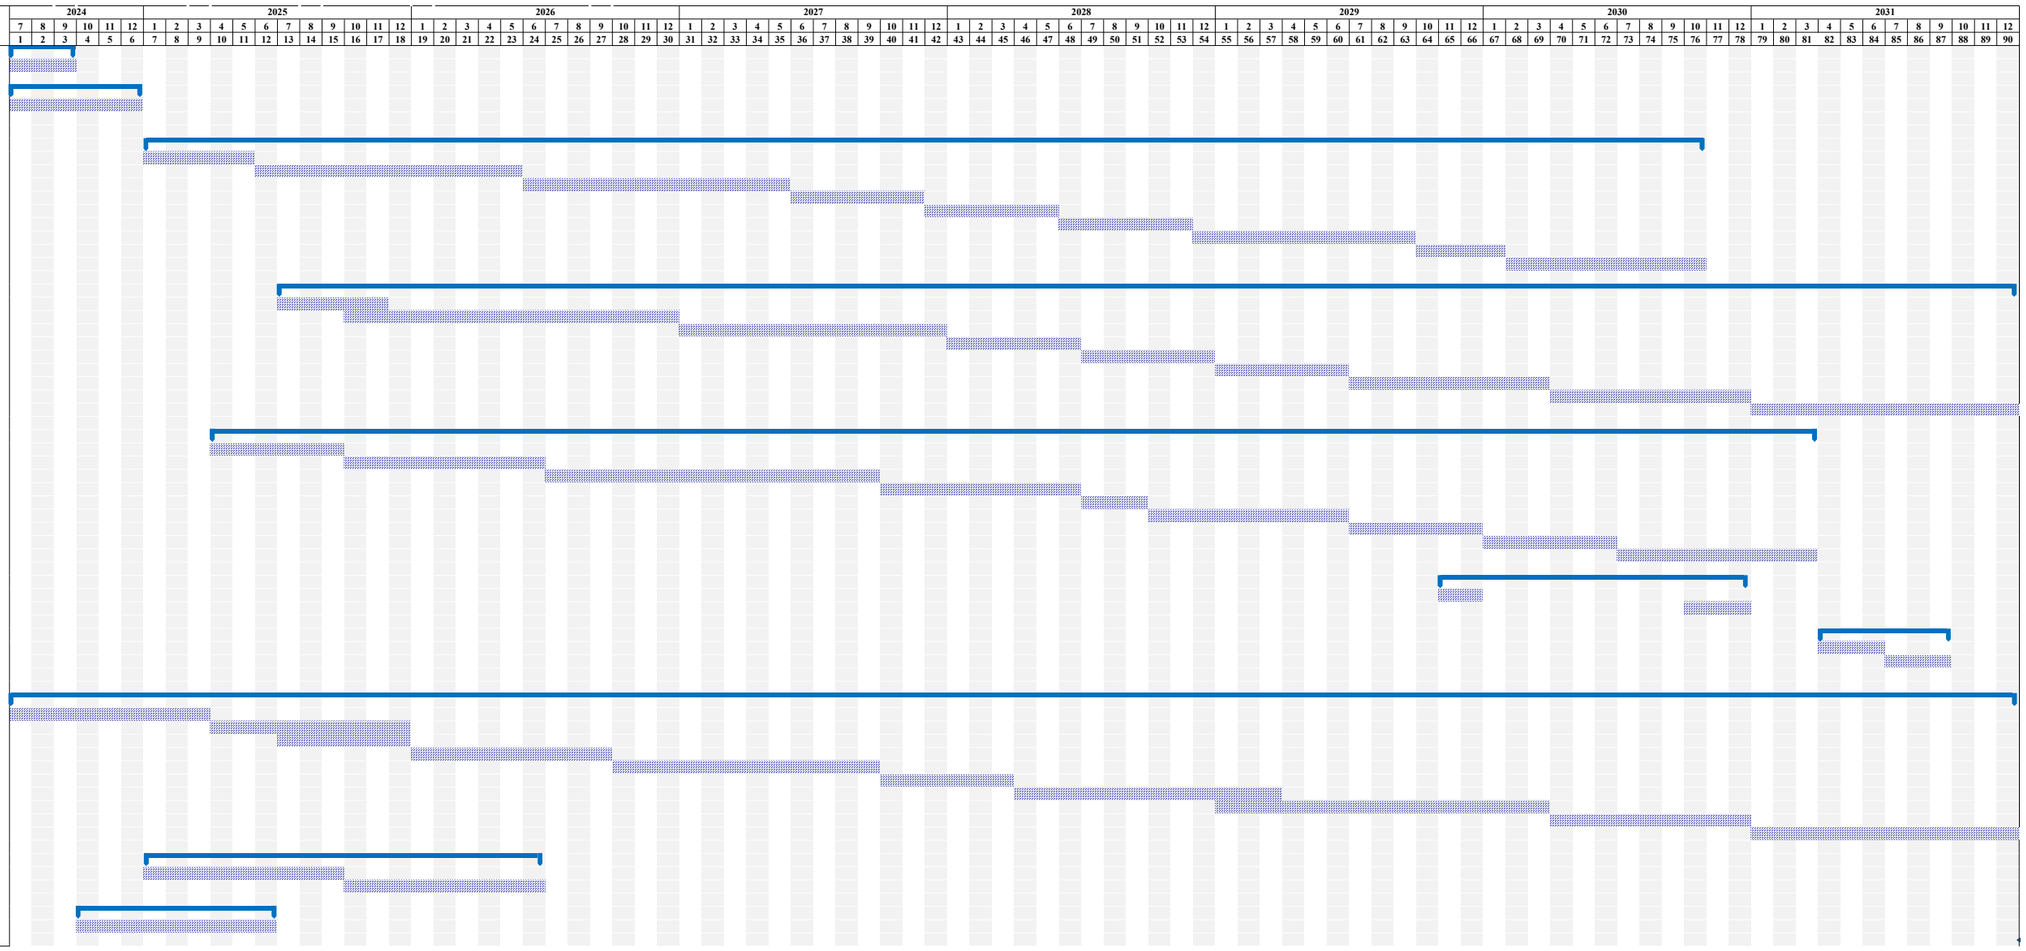
ID	Activity
1	**XP & TTM Application**
2	**Tree Felling and/or Site Clearance**
3	**Lung Fu Road Slip Road**
	3a - LFR Viaduct (North Section)
	(i) Predrilling
	(ii) UU Diversion
	(iii) Piling
	(iv) ELS
	(v) Pile Caps
	(vi) Abutment & Piers, and Reinstatement of Slope
	(vii) Bridge Deck
	(viii) Noise Barriers, Street Lighting, Street Furniture, Road Surfacing & Road Marking
	(ix) Landscape and Establishment Works
	3b - LFR Viaduct (South Section)
	(i) Predrilling
	(ii) UU Diversion
	(iii) Piling
	(iv) ELS
	(v) Pile Caps
	(vi) Abutment & Piers, and Reinstatement of Slope
	(vii) Bridge Deck
	(viii) Noise Barriers, Street Lighting, Street Furniture, Road Surfacing & Road Marking
	(ix) Landscape and Establishment Works
	3c - Slip Road between TWR & WCR
	(i) Predrilling
	(ii) ELS
	(iii) Piling (Stage 1 - At Ex. Slopes)
	(iv) Retaining Walls and U-troughs (Stage 1)
	(v) Formation of Temp. Road for Traffic Diversion
	(vi) Piling (Stage 2 - At Ex. Slip Road)
	(vii) Retaining Walls and U-troughs (Stage 2)
	(viii) Street Lighting, Street Furniture, Road Surfacing & Road Marking
	(ix) Landscape and Establishment Works
	3d - TWR adjacent to Tsing Shan Tsuen LRT Station
	(i) Street Lighting, Street Furniture, Road Surfacing & Road Marking
	(ii) Landscape and Establishment Works
	3e - Road Intersection of Lung Mun Road near Glorious Garden
	(i) Street Lighting, Street Furniture, Road Surfacing & Road Marking
	(ii) Landscape and Establishment Works
4	**Hoi Wing Road Slip Road and Junction Improvement of Castle Peak Road**
	4a - Hoi Wing Road Slip Road
	(i) Boulder Survey
	(ii) Predrilling
	(iii) UU Diversion, Removal and Reprovision of Staircase
	(iv) ELS Works (Stage 1 - For Piling Works)
	(v) Piling (Bored Piles)
	(vi) Piling (Socketed H-piles)
	(vii) ELS Works (Stage 2 - For U-trough Construction)
	(viii) U-trough Structure
	(ix) Street Lighting, Street Furniture, Road Surfacing & Road Marking
	(x) Landscape and Establishment Works
	4b - Junction Improvement Works between Hoi Wing Road and Castle Peak Road
	(i) UU Diversion
	(ii) Junction Improvement Works
	4c - Junction Improvement Works between Sam Shing Street and Castle Peak Road
	(i) Junction Improvement Works
